

# 港鐵東涌綫延綫 社區聯絡小組(西段)

第七次會議

日期: 30-12-2024

# 議程

1. 現有東涌站的相關工程
2. 東涌西段及車站建造工程進度
3. 東堤灣畔工地工程進度及隧道鑽挖機組件運送
4. 未來六個月臨時交通管理措施
5. 環境監察及審核
6. 查詢及投訴摘要
7. 社區聯繫
8. 其他事項及下次會議日程

# 工程進度

# 項目進度

2025年第1季:

- 東涌東段 - 新路軌建造及改道工程
- 東涌東站 - 車站月台及大堂結構工程
- 東涌西段 - 隧道鑽挖機泥漿處理設施建造工程
- 東涌西站 - 地底連續牆建造工程



2023-2024

展開建造工程

進行工地平整及  
地基工程



2024-2027

進行車站土木工程

進行東涌西段隧道  
鑽挖工程

東段改道工程



2027-2028

進行機電及裝修  
工程

各項測試及試營運






2029

竣工

# 首次關鍵道岔安裝工序已於10月26日順利完成

調整服務當晚…

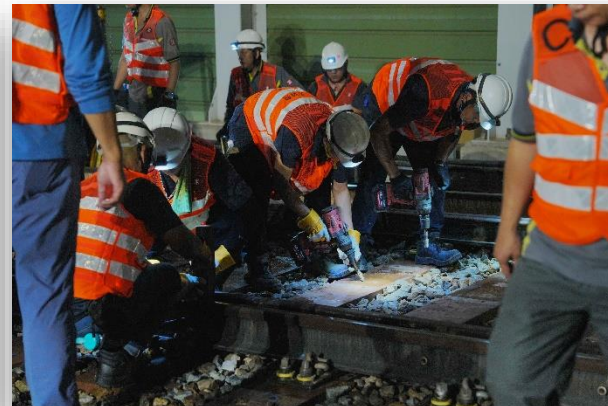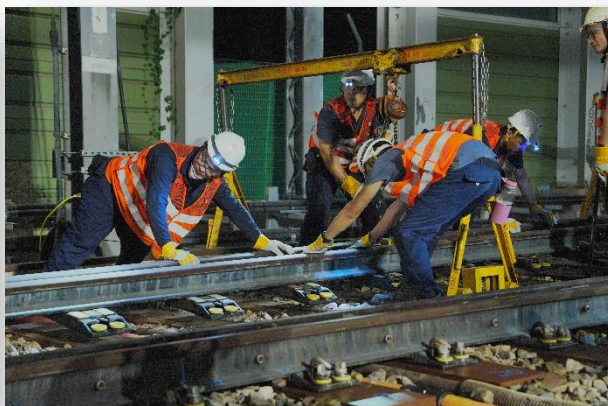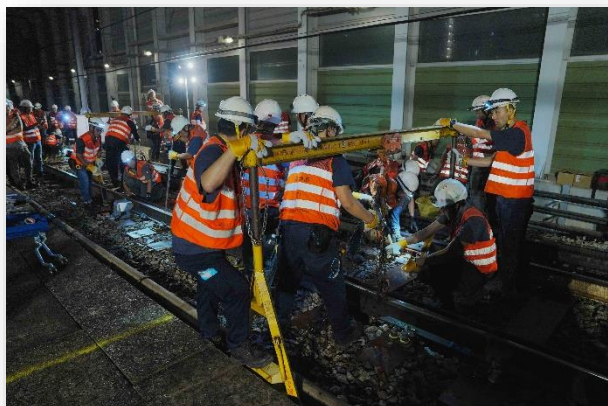


✓ 完成一連串繁複工序，包括安裝路軌組件、調校路軌位置並進行連接、安裝轉轍器等、進行各項測試




✓ 安排免費接駁巴士返往東涌及欣澳站、共動員超過100名人手協助乘客、增設特別標示和指示牌

# 現有東涌站相關改動

- ❖ 於東涌站天台及月台的機房，進行機械及設備安裝 (進行中)
- ❖ 於掉頭隧道進行改動 (進行中)

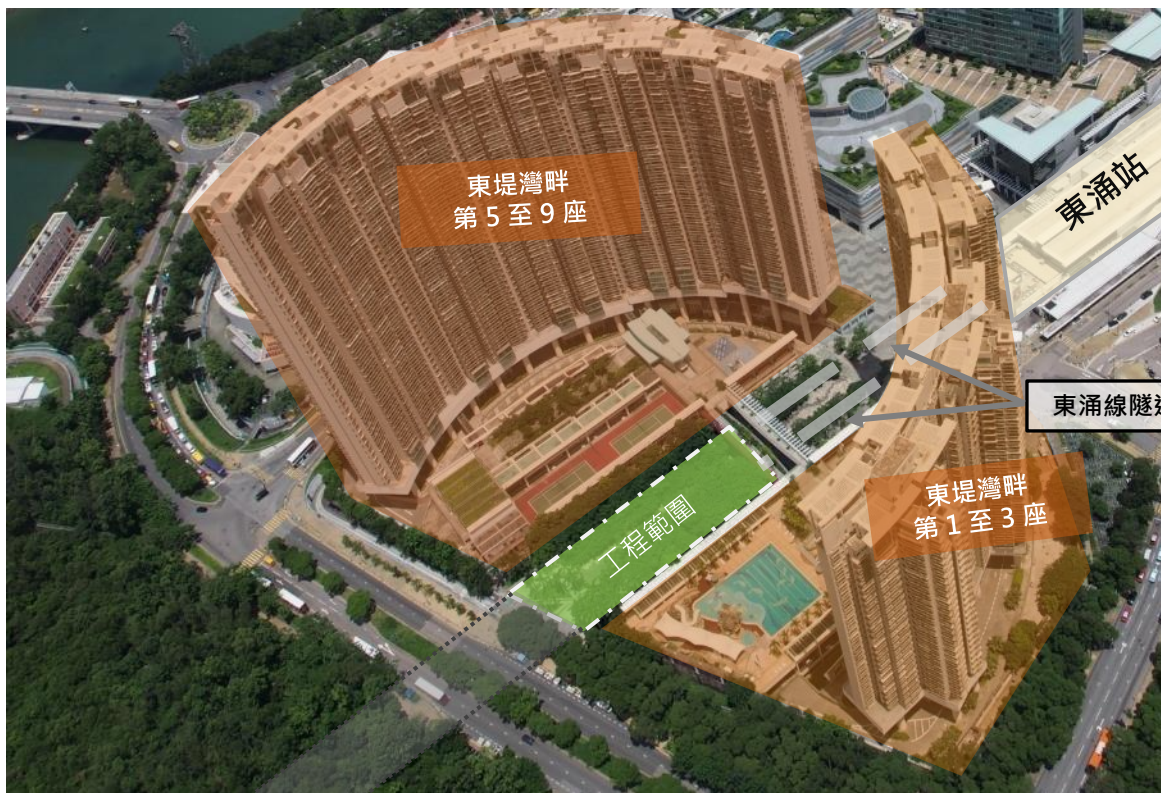

東涌站掉頭隧道方向

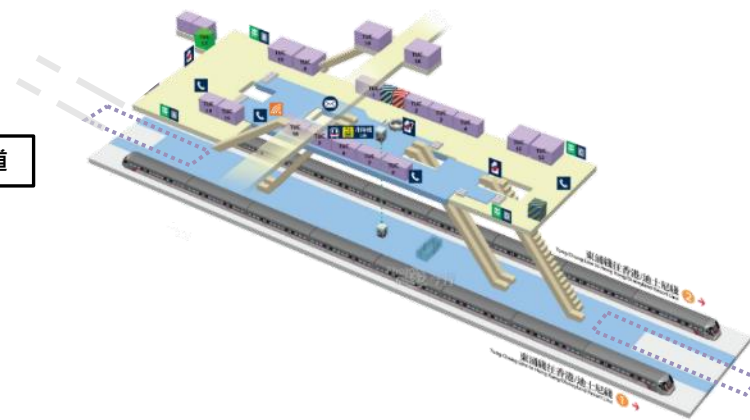

列車行車方向

# 東涌西段 - 工程進度



臨時隔音罩建造工程 (已完成)



隧道鑽挖機泥漿處理設施  
(大致完成)



東涌西站連續間牆建造工程 (進行中)

# 東涌西站 - 工程進度






# 東涌西段工程進度

- ❖ 西段總承建商: 布依格 - 寶嘉1201聯營
- ❖ 東堤灣畔工地的臨時隔音罩建造工程 (已完成)
- ❖ 於順東路山邊設置泥漿處理設施 (大致完成)
- ❖ 東涌西站的連續間牆工程 (進行中)
- ❖ 於馬灣涌村進行建築物監測 (進行中)
- ❖ 於馬灣涌村進行施工前樓宇現況勘察 (進行中)
- ❖ 隧道鑽挖機組件運送及組裝 (進行中)


# 未來六個月工程安排 及 臨時交通管理措施

# 隧道鑽挖機組件運送

運送次數 (共9個晚上)	運送日期 (01:00-05:00)
試運、第一至第七運	已於2024年11月至12月完成
第八、九運	預計2025年第二季完成

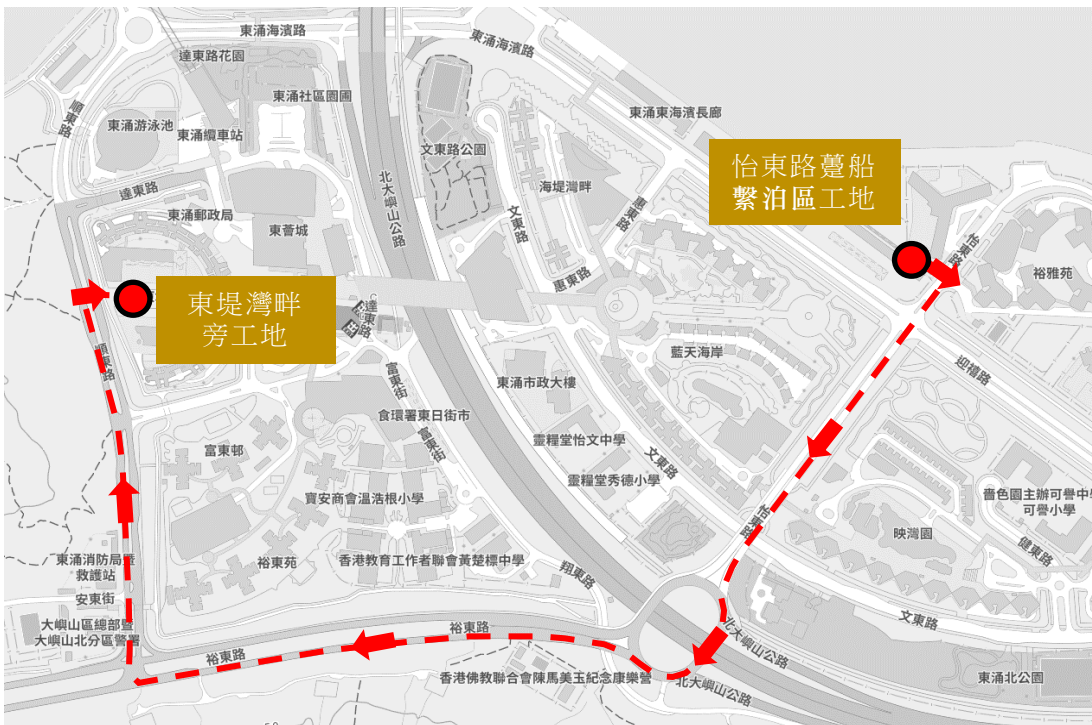

運送車隊途經順東路

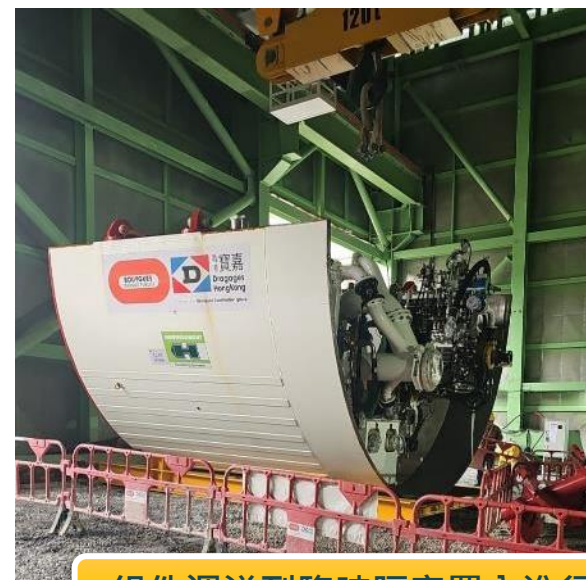

組件運送到臨時隔音罩內進行安裝


# 順東路山邊設置隧道鑽挖機泥漿處理設施




# 順東路臨時交通管理措施



# 裕東路臨時交通管理措施

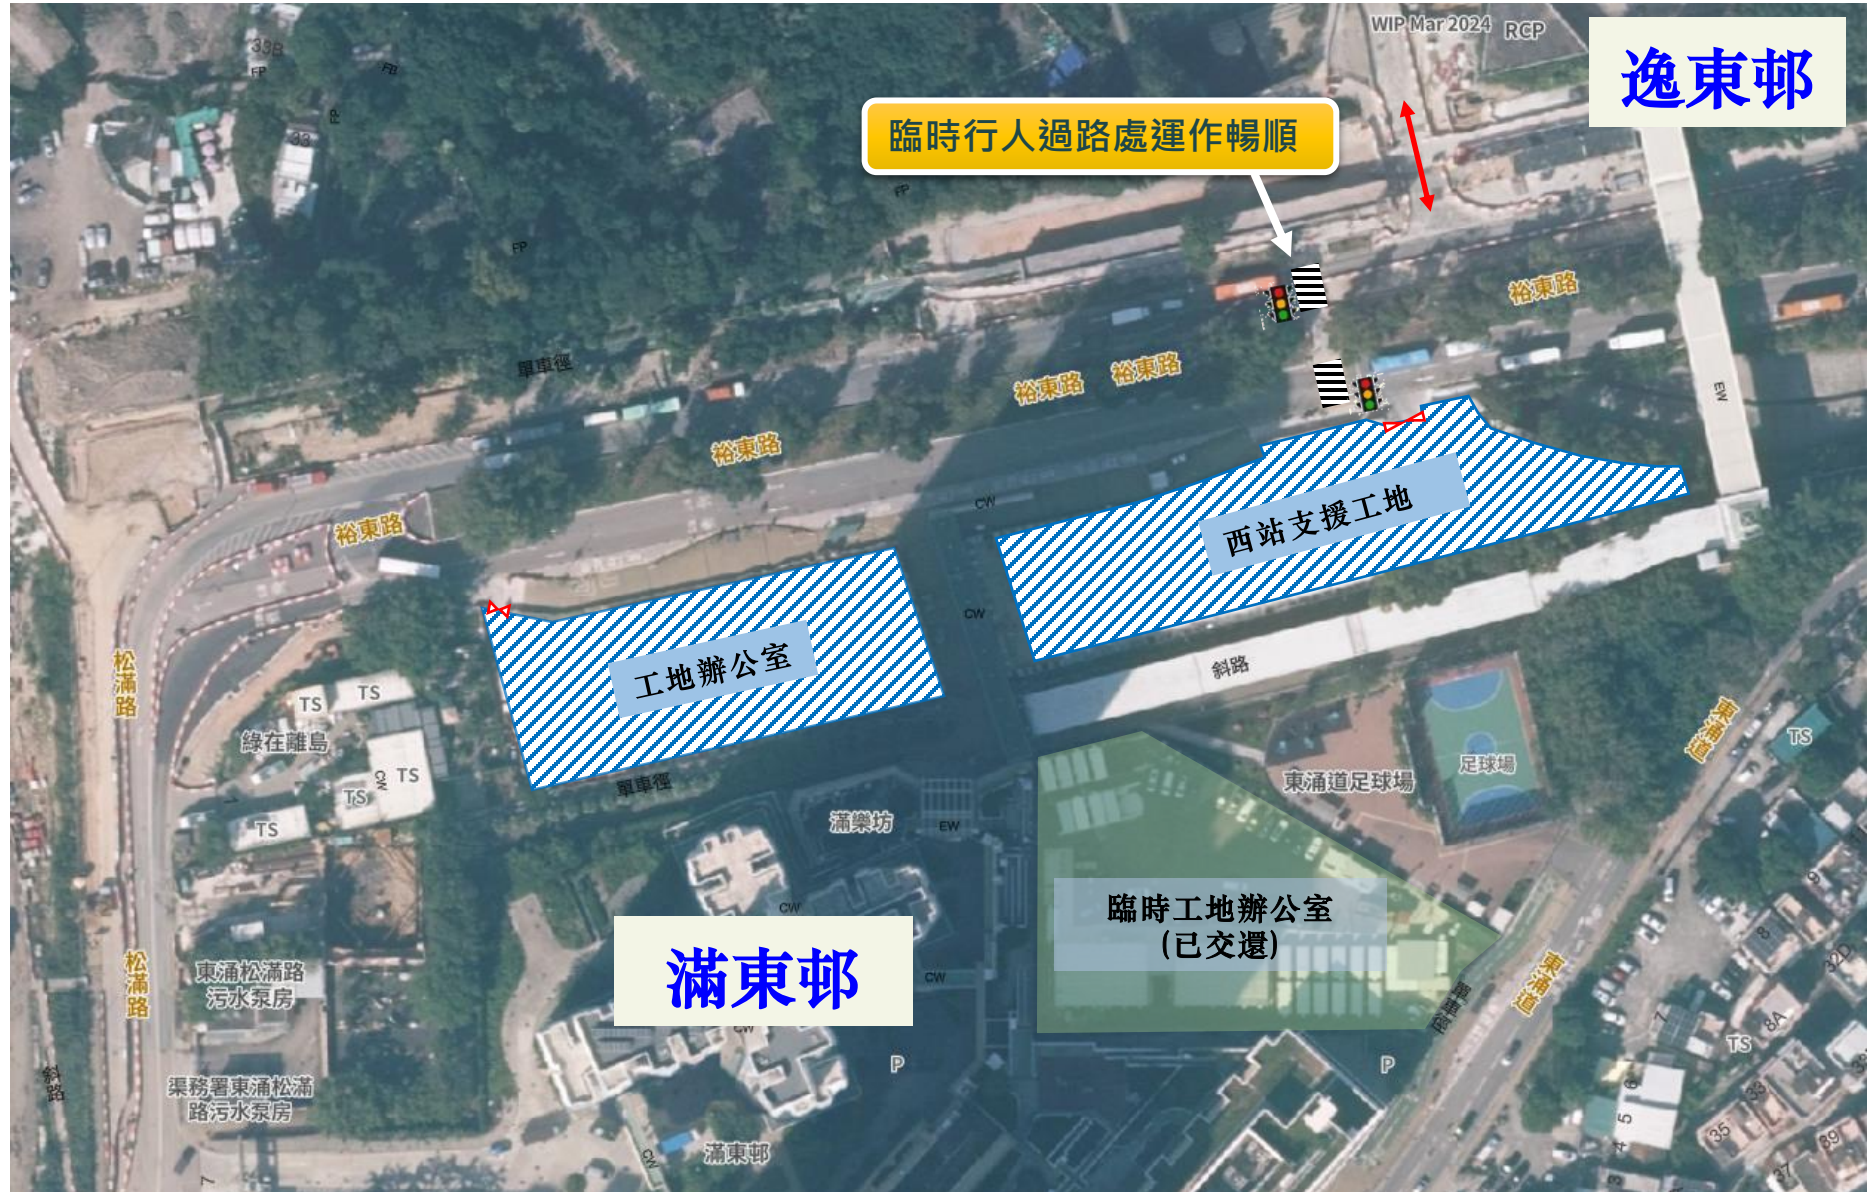

# 怡東路臨時躉船起卸設施及躉船繫泊區

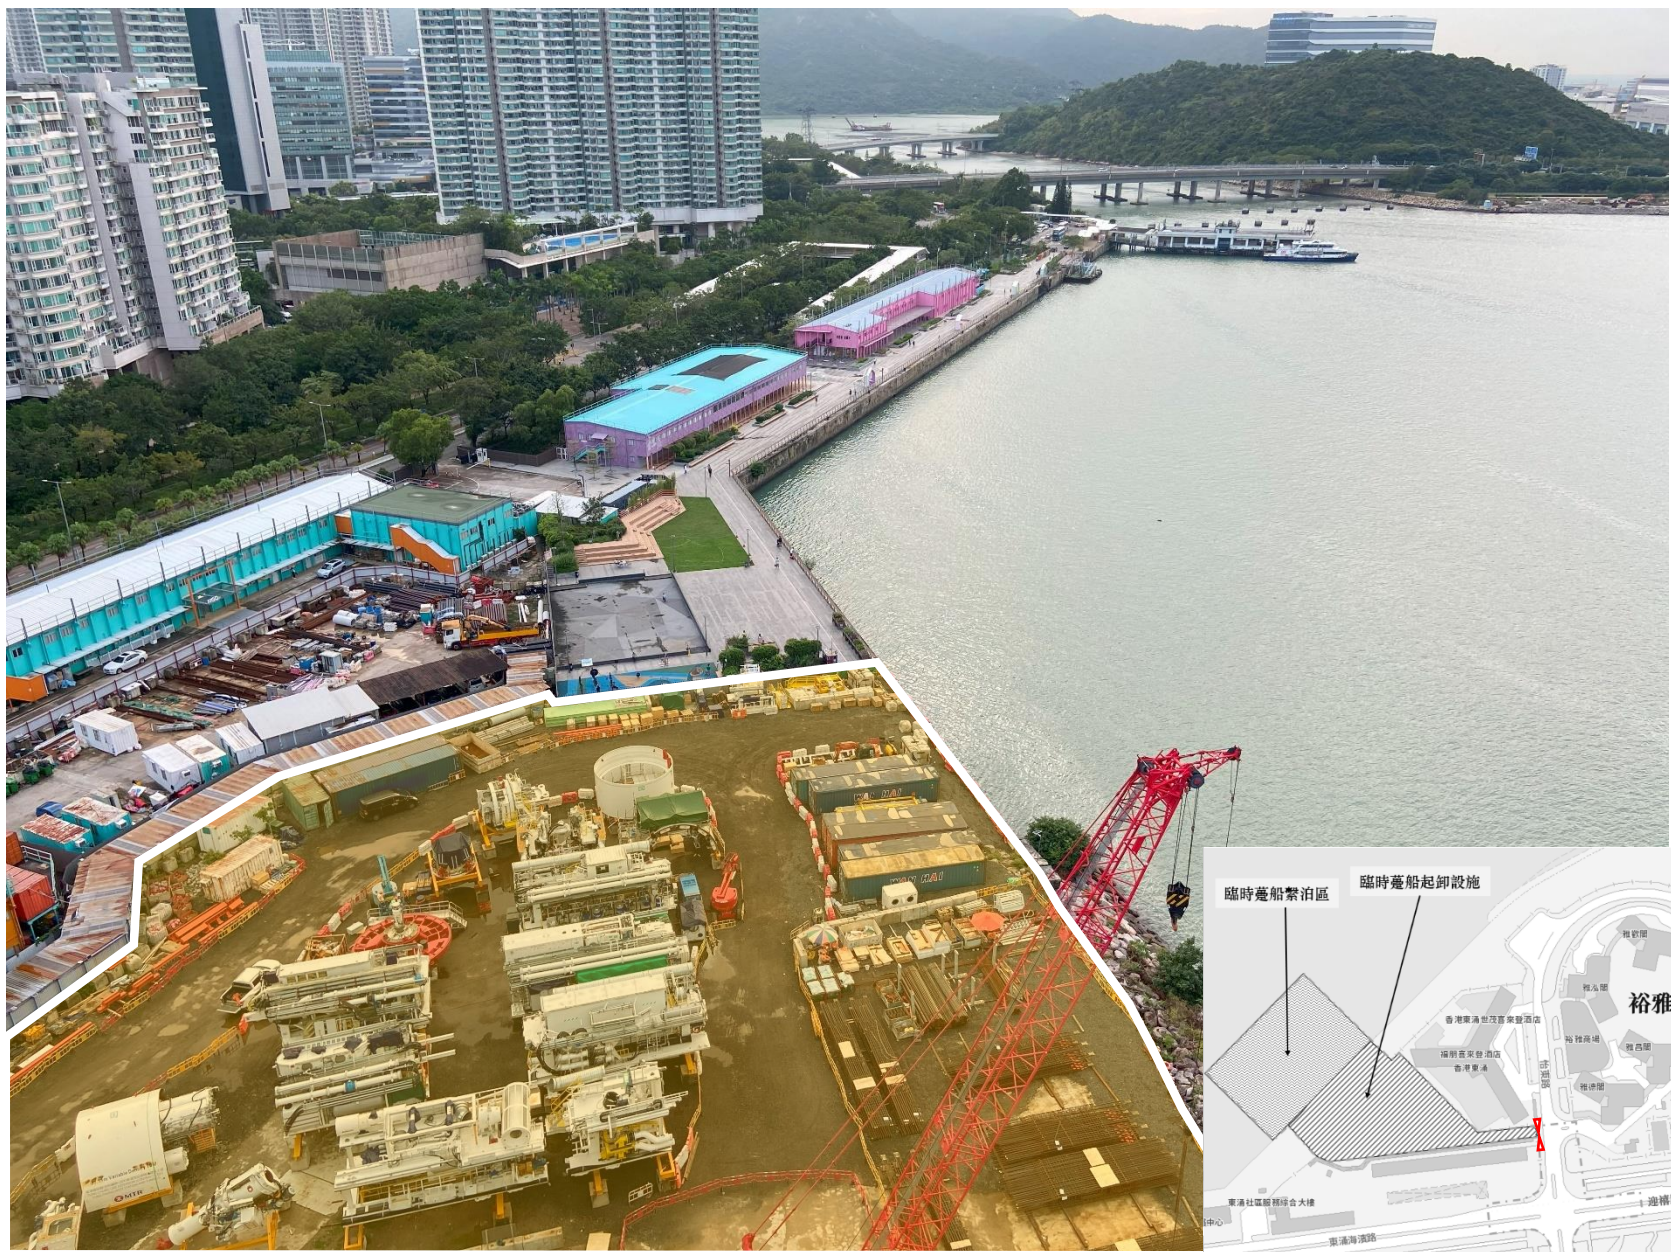

# 於馬灣涌村進行建築物監測





# 於馬灣涌村進行施工前樓宇現況勘察



## 馬灣涌村工程告示



## 滿東邨旁工程資訊板



### 東堤灣畔工程資訊板

- 《東涌·言綫》工程通訊
- 隧道鑽挖機組件運送安排

# 環境監察及審核

# 環境監察及審核

www.mtrtungchunglineextension.hk

## 環境監察及審核數據相關網站

The screenshot shows the MTR Tung Chung Line Extension website. The top navigation bar includes the MTR logo, the slogan 'Go smart Go beyond', and the website name '東涌綫延綫'. There are links for 'Home', 'Explore Tung Chung Line Extension', 'Engineering Information', 'Community Engagement', and 'Information Centre'. A dropdown menu is open under 'Engineering Information', with 'Engineering Safety and Environmental Protection' highlighted. The main content area features a large image of the project and a section titled '環境保護' (Environment Protection). Below this, there is a section for '環境影響評估' (Environmental Impact Assessment) and '環境監測' (Environmental Monitoring). A '請按此' (Click here) button with a hand icon is positioned below the 'Environment Monitoring' section.

### 環境監察及審核結果:

- 空氣質素及噪音監測均沒有超標記錄

This screenshot shows the 'Noise Monitoring Data' section of the website. It features a header with the MTR logo and slogan, followed by the project name 'TUNG CHUNG LINE EXTENSION'. A navigation menu includes 'Home', 'EIAO Documents', 'EP Submissions', 'Air Quality Monitoring Data', 'Noise Monitoring Data', and 'EM&A Reports'. Below the menu, there are dropdown menus for 'Station', 'Year', and 'Month', all set to 'All'. There are 'Search' and 'Reset' buttons.

This screenshot shows the 'Air Quality Monitoring Data' section of the website. It features a header with the MTR logo and slogan, followed by the project name 'TUNG CHUNG LINE EXTENSION'. A navigation menu includes 'Home', 'EIAO Documents', 'EP Submissions', 'Air Quality Monitoring Data', 'Noise Monitoring Data', and 'EM&A Reports'. Below the menu, there are dropdown menus for 'Station', 'Year', and 'Month', all set to 'All'. There are 'Search' and 'Reset' buttons.


# 環境緩解措施



使用臨時隔音屏障



妥善儲存化學廢物

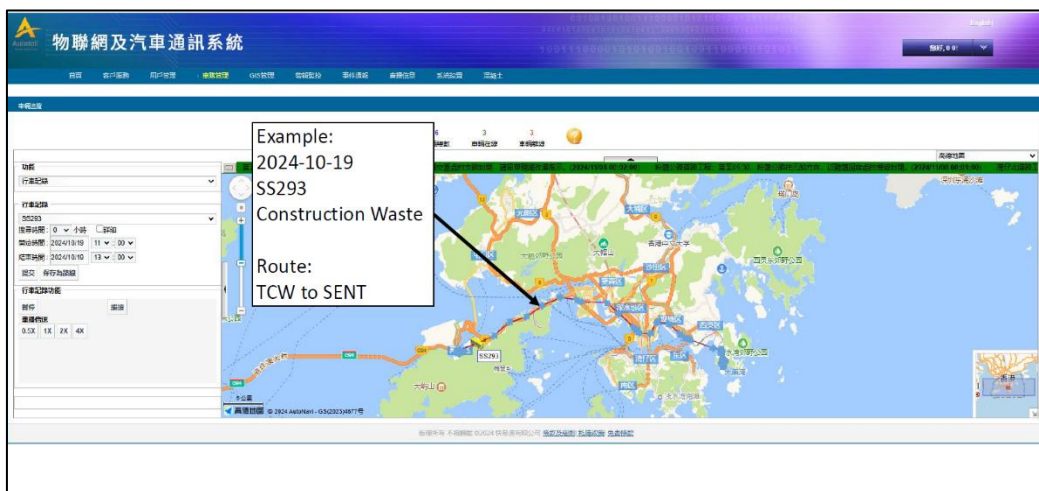

實時監測泥頭車行駛路線



安排工程期間灑水

# 查詢及投訴摘要

截至2024年12月底

	空氣	噪音	污水管理	有關樹木/ 植物	路面不平	其他*
查詢及投訴次數	18	64	6	12	6	32
(上次會議 匯報次數)	14	55	4	12	6	28
相關的檢控	0	0	0	0	0	0

\*包括: 臨時交通管理措施, 工地管理, 查詢工程安排、項目設計等

## 聯絡方法

- 承建商熱線-東堤灣畔工地範圍(地盤主管-鄧先生)(6652 7836)
- 承建商熱線-東涌西站工地範圍(首席地盤總管-吳先生)(6180 8187)
- 港鐵工程熱線(2993 3333)
- 電郵:[newprojects@mtr.com.hk](mailto:newprojects@mtr.com.hk)

# 社區聯繫

## 地區聯繫



地區關愛隊探訪活動

與東堤灣畔業主會見面

## 項目宣傳/ 資訊



學校及社區講座 -  
新鐵路項目青年大使計劃



東涌綫延綫實體  
資訊中心



第四期  
《東涌。言綫》

# 其他事項
